U-PMS Rollout Plan

How to schedule it, step by step, in U-PMS and in Jira, so you can compare the two tools.

Prepared: 15 October 2026 **Plan span:** 27 Sep 2026 to 10 Mar 2027 **Work items:** 10 epics, 49 tasks and stories, 42 sub-tasks

1. How to use this guide

- **Section 2** shows how the plan is organised: milestones become epics, steps become tasks, and finer steps become sub-tasks.
- **Section 3** shows the schedule at a glance. **Section 4** lists every work item with its dates, labels and dependencies, ready to enter.
- **Section 5** gives the same steps side by side for U-PMS and Jira. Do each step in both tools.
- **Section 6** is a checklist to note what you find easier, faster or missing in each tool.

> **The dates are proposals.** They assume 5-day working weeks, no public holidays, and that the parallel tracks start the Monday after the IT-PMO approval. Change them to match your real commitments before you enter them.

2. Plan structure

One space, four levels


Level	Used for	Example
Space	The whole rollout	U-PMS Rollout
Epic	Each of the 10 milestones	3. UAT
Task / Story	Each step of a milestone (child work item of the epic)	Deploy U-PMS to the UAT VM
Sub-task	A smaller step inside a task	Get the form signed by the Head of Department

Stories are used for building work (features); tasks for actions such as forms, tickets and approvals.

Conventions

- **Dates:** every task has a start date and a due date; an epic spans its tasks.
- **Dependencies:** "waits for" links (Jira: "is blocked by") show the order and draw arrows on the Timeline.
- **Teams as labels:** external teams have no accounts, so each task carries a team label: wan-core ms-team data-team bpm iam ea is it-pmo . Other labels: development testing uat deployment security approval production documentation .
- **Assignee:** you, as the owner who follows up with each team.
- **Status:** the finished development phases are DONE ; everything else starts in TO DO .

Milestone flow

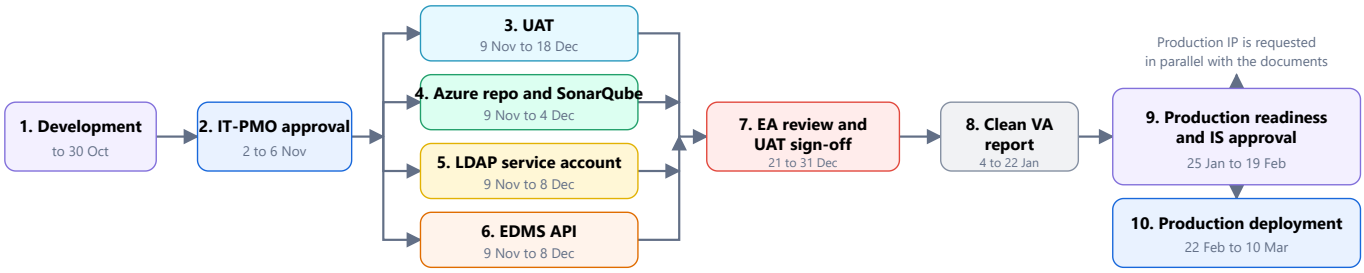

Milestones 3 to 6 run in parallel after the IT-PMO approval. Milestone 7 starts when UAT testing, the SonarQube report and the EDMS work are finished.

3. Schedule at a glance

Each row is one epic (bold) or task, drawn from its start date to its due date. The red line is today, 15 October 2026.

Work item	Oct 2026	Nov	Dec	Jan 2027	Feb	Mar
1. Development						
1.1 Phase 1: core Kanban space						
1.2 Phase 2: space views and team						
1.3 Phase 3: templates and planning						
1.4 Phase 4: collaboration and search						
1.5 Jira parity pass						
1.6 Blank space: Jira views and look						
1.7 Update automated tests for the ne…						
1.8 Validate Phase 3: browser tests, perf…						
1.9 Validate Phase 4: browser tests, perf…						
1.10 Validate the Jira parity pass: brows…						
1.11 Restyle the Scrum and Kanban te…						
1.12 Security and code review of the ne…						
1.13 Release build and deployment pac…						
2. IT-PMO approval						
2.1 Submit U-PMS to the IT-PMO depa…						
2.2 Get approval from the IT-PMO dep…						
3. UAT						
3.1 Get the UAT VM IP from the WAN C…						
3.2 Fill out the TDL user creation form a…						
3.3 Raise a BPM ticket for NAF to reach…						
3.4 Deploy U-PMS to the UAT VM						
3.5 UAT testing						
4. Azure repository and SonarQube						
4.1 Ask the Data team to create the Az…						
4.2 Get the repository IP from the Data …						
4.3 Raise a BPM ticket for NAF to the A…						
4.4 Push the code to the Azure reposit…						
4.5 Get the SonarQube report from the…						



4. Work breakdown

Enter the items in this order. The ID (for example **3.4**) is only for this guide; each tool gives its own key (UPR-12, and so on). "Waits for" lists the items that must finish first.

1. Development

27 Sept to 30 Oct · Epic · IN PROGRESS

Build U-PMS. The built phases are done; the remaining checks are to do.

ID	Type	Work item	Start	Due	Status	Labels	Waits for
1.1	Story	Phase 1: core Kanban space	27 Sept	28 Sept	DONE	development	-
	Sub-task	Sign-in, accounts and administration	27 Sept	28 Sept	DONE		
	Sub-task	Kanban board and columns	27 Sept	28 Sept	DONE		
	Sub-task	Work item details, comments and history	27 Sept	28 Sept	DONE		
	Sub-task	Permissions, audit log and security hardening	27 Sept	28 Sept	DONE		
1.2	Story	Phase 2: space views and team	28 Sept	30 Sept	DONE	development	-
	Sub-task	Teams and members-only spaces	28 Sept	30 Sept	DONE		
	Sub-task	Assignees, dates, board filters and My tasks	28 Sept	30 Sept	DONE		
	Sub-task	List view	28 Sept	30 Sept	DONE		
	Sub-task	Timeline view	28 Sept	30 Sept	DONE		
1.3	Story	Phase 3: templates and planning	28 Sept	1 Oct	DONE	development	-
	Sub-task	Scrum template: backlog and sprints	28 Sept	1 Oct	DONE		
	Sub-task	Stage-gate template: stages and gate approvals	28 Sept	1 Oct	DONE		
	Sub-task	Epics, stories, bugs and milestones	28 Sept	1 Oct	DONE		
	Sub-task	Dependencies between work items	28 Sept	1 Oct	DONE		
1.4	Story	Phase 4: collaboration and search	1 Oct	7 Oct	DONE	development	-
	Sub-task	Formatted text and mentions	1 Oct	7 Oct	DONE		
	Sub-task	Watchers, notifications and email outbox	1 Oct	7 Oct	DONE		
	Sub-task	Attachments with malware check	1 Oct	7 Oct	DONE		
	Sub-task	Labels, search and saved filters	1 Oct	7 Oct	DONE		
1.5	Story	Jira parity pass	7 Oct	12 Oct	DONE	development	-
	Sub-task	Spaces and the Create space flow	7 Oct	12 Oct	DONE		
	Sub-task	Global Create form	7 Oct	12 Oct	DONE		
	Sub-task	Board columns managed on the board	7 Oct	12 Oct	DONE		
	Sub-task	Template gallery and Blank template	7 Oct	12 Oct	DONE		
	Sub-task	Jira layout: sidebar, Summary page and swimlanes	7 Oct	12 Oct	DONE		
1.6	Story	Blank space: Jira views and look	13 Oct	15 Oct	DONE	development	-
	Sub-task	Calendar view	13 Oct	15 Oct	DONE		
	Sub-task	Attachments, Reports and Archived work items	13 Oct	15 Oct	DONE		
	Sub-task	Approvals, Forms and Docs	13 Oct	15 Oct	DONE		
	Sub-task	Space tabs, Shortcuts, Share and Full screen	13 Oct	15 Oct	DONE		

ID	Type	Work item	Start	Due	Status	Labels	Waits for
	Sub-task	Summary, Reports and Timeline in Jira's layout	13 Oct	15 Oct	DONE		
1.7	Task	Update automated tests for the new Timeline and Archived pages	16 Oct	19 Oct	TO DO	development, testing	-
1.8	Task	Validate Phase 3: browser tests, performance run and manual checks	16 Oct	20 Oct	TO DO	testing	-
1.9	Task	Validate Phase 4: browser tests, performance run and manual checks (T097-T104)	19 Oct	22 Oct	TO DO	testing	-
1.10	Task	Validate the Jira parity pass: browser, performance, quickstart, screen reader (T088-T098)	21 Oct	26 Oct	TO DO	testing	-
1.11	Story	Restyle the Scrum and Kanban templates like Jira	22 Oct	28 Oct	TO DO	development	-
1.12	Task	Security and code review of the new space pages	27 Oct	28 Oct	TO DO	development, security	-
1.13	Task	Release build and deployment package for UAT	29 Oct	30 Oct	TO DO	development, deployment	1.7, 1.8, 1.9, 1.10, 1.11, 1.12

2. IT-PMO approval

2 Nov to 6 Nov · Epic · TO DO

Get the IT-PMO department's approval before UAT.

ID	Type	Work item	Start	Due	Status	Labels	Waits for
2.1	Task	Submit U-PMS to the IT-PMO department for approval	2 Nov	3 Nov	TO DO	it-pmo	1.13
2.2	Task	Get approval from the IT-PMO department	4 Nov	6 Nov	TO DO	it-pmo, approval	2.1

3. UAT

9 Nov to 18 Dec · Epic · TO DO

User acceptance testing on a UAT virtual machine.

ID	Type	Work item	Start	Due	Status	Labels	Waits for
3.1	Task	Get the UAT VM IP from the WAN Core team	9 Nov	11 Nov	TO DO	wan-core, uat	2.2
3.2	Task	Fill out the TDL user creation form and submit it to the MS team	9 Nov	13 Nov	TO DO	ms-team, uat	2.2
	Sub-task	Fill out the TDL user creation form	9 Nov	13 Nov	TO DO		
	Sub-task	Submit the form to the MS team	9 Nov	13 Nov	TO DO		
3.3	Task	Raise a BPM ticket for NAF to reach the UAT VM from the local system	12 Nov	18 Nov	TO DO	bpm, uat	3.1
3.4	Task	Deploy U-PMS to the UAT VM	19 Nov	25 Nov	TO DO	deployment, uat	3.2, 3.3
3.5	Task	UAT testing	9 Dec	18 Dec	TO DO	testing, uat	3.4, 5.5
	Sub-task	Prepare the UAT test cases	9 Dec	18 Dec	TO DO		
	Sub-task	Run UAT with the business users	9 Dec	18 Dec	TO DO		
	Sub-task	Fix the UAT findings	9 Dec	18 Dec	TO DO		

4. Azure repository and SonarQube

9 Nov to 4 Dec · Epic · TO DO

In parallel with UAT: the code goes to the Data team's Azure repository and is scanned by SonarQube.

ID	Type	Work item	Start	Due	Status	Labels	Waits for
4.1	Task	Ask the Data team to create the Azure repository	9 Nov	13 Nov	TO DO	data-team	2.2
4.2	Task	Get the repository IP from the Data team	16 Nov	18 Nov	TO DO	data-team	4.1
4.3	Task	Raise a BPM ticket for NAF to the Azure repository	19 Nov	25 Nov	TO DO	bpm	4.2
4.4	Task	Push the code to the Azure repository	26 Nov	27 Nov	TO DO	development	4.3
4.5	Task	Get the SonarQube report from the Data team	30 Nov	4 Dec	TO DO	data-team security	4.4

5. LDAP service account

9 Nov to 8 Dec · Epic · TO DO

In parallel with UAT: the IAM team creates a service account; the MS team provides the LDAP APIs for UAT.

ID	Type	Work item	Start	Due	Status	Labels	Waits for
5.1	Task	Fill out the IAM service account form	9 Nov	12 Nov	TO DO	iam	2.2
	Sub-task	Fill out the service account form	9 Nov	12 Nov	TO DO		
	Sub-task	Get the form signed by the Head of Department	9 Nov	12 Nov	TO DO		
5.2	Task	Raise the service account ticket on BPM (New ACMS)	13 Nov	18 Nov	TO DO	bpm iam	5.1
	Sub-task	Raise the ticket in New ACMS	13 Nov	18 Nov	TO DO		
	Sub-task	Get the ticket approved by the Head of Department	13 Nov	18 Nov	TO DO		
5.3	Task	IAM team creates the service account	19 Nov	27 Nov	TO DO	iam	5.2
5.4	Task	Email the service account credentials to the MS team	30 Nov	1 Dec	TO DO	ms-team	5.3
5.5	Task	MS team provides the LDAP APIs for UAT	2 Dec	8 Dec	TO DO	ms-team uat	5.4

6. EDMS API

9 Nov to 8 Dec · Epic · TO DO

In parallel with UAT: the BPM team provides the EDMS API to save the application's documents.

ID	Type	Work item	Start	Due	Status	Labels	Waits for
6.1	Task	Raise the IT work form on BPM	9 Nov	13 Nov	TO DO	bpm	2.2
6.2	Task	Get the EDMS API from the BPM team	16 Nov	27 Nov	TO DO	bpm	6.1
6.3	Story	Save application documents through the EDMS API	30 Nov	8 Dec	TO DO	development	6.2

7. EA review and UAT sign-off

21 Dec to 31 Dec · Epic · TO DO

After UAT and the parallel tracks: the Enterprise Architecture review and the UAT sign-off that IS approval needs.

ID	Type	Work item	Start	Due	Status	Labels	Waits for
7.1	Task	Ask the Enterprise Architecture team to evaluate U-PMS	21 Dec	23 Dec	TO DO	ea	3.5, 4.5, 6.3
7.2	Task	Get the EA diagram from the EA team	24 Dec	31 Dec	TO DO	ea	7.1
7.3	Task	Get the UAT sign-off (needed for IS approval)	21 Dec	24 Dec	TO DO	uat approval	3.5

8. Clean VA report

4 Jan 2027 to 22 Jan 2027 · Epic · TO DO

The MS team installs the scan agent; IS scans the VM and reports vulnerabilities until the report is clean.

ID	Type	Work item	Start	Due	Status	Labels	Waits for
8.1	Task	Ask the MS team to install the scan agent on the VM	4 Jan 2027	6 Jan 2027	TO DO	ms-team security	7.3
8.2	Task	IS runs the vulnerability scan	7 Jan 2027	13 Jan 2027	TO DO	is security	8.1
8.3	Task	Fix the vulnerabilities found	14 Jan 2027	20 Jan 2027	TO DO	development security	8.2
8.4	Task	Get the clean VA report from IS	21 Jan 2027	22 Jan 2027	TO DO	is security	8.3

9. Production readiness and IS approval

25 Jan 2027 to 19 Feb 2027 · Epic · TO DO

The production IP, and the documents IS needs for its approval.

ID	Type	Work item	Start	Due	Status	Labels	Waits for
9.1	Task	Ask the WAN Core team for the production IP	25 Jan 2027	29 Jan 2027	TO DO	wan-core production	8.4
9.2	Task	Prepare the IS approval documents	25 Jan 2027	5 Feb 2027	TO DO	is documentation	8.4, 7.2, 4.5
	Sub-task	BRD	25 Jan 2027	5 Feb 2027	TO DO		
	Sub-task	FSD	25 Jan 2027	5 Feb 2027	TO DO		
	Sub-task	API document	25 Jan 2027	5 Feb 2027	TO DO		
	Sub-task	Clean VA report	25 Jan 2027	5 Feb 2027	TO DO		
	Sub-task	SonarQube report	25 Jan 2027	5 Feb 2027	TO DO		
	Sub-task	Release note	25 Jan 2027	5 Feb 2027	TO DO		
	Sub-task	EA diagram	25 Jan 2027	5 Feb 2027	TO DO		
9.3	Task	Submit the documents to IS and get IS approval	8 Feb 2027	19 Feb 2027	TO DO	is approval	9.2

10. Production deployment

22 Feb 2027 to 10 Mar 2027 · Epic · TO DO

Production access and settings from the MS team, then the go-live deployment.

ID	Type	Work item	Start	Due	Status	Labels	Waits for
10.1	Task	Get production database access from the MS team	22 Feb 2027	26 Feb 2027	TO DO	ms-team, production	9.3
10.2	Task	Get the SSL certificate from the MS team	22 Feb 2027	26 Feb 2027	TO DO	ms-team, production	9.3
10.3	Task	Get the production SMTP details from the MS team	22 Feb 2027	26 Feb 2027	TO DO	ms-team, production	9.3
10.4	Task	Get the production LDAP details from the MS team	22 Feb 2027	26 Feb 2027	TO DO	ms-team, production	9.3
10.5	Task	Configure the database, SSL, SMTP and LDAP for production	1 Mar 2027	5 Mar 2027	TO DO	development, production	10.1, 10.2, 10.3, 10.4
10.6	Task	Deploy U-PMS to production	8 Mar 2027	10 Mar 2027	TO DO	deployment, production	10.5, 9.1

5. Step by step in U-PMS and in Jira

Both columns reach the same result. The Jira steps are for a Jira Cloud team-managed space; menu names can differ slightly between Jira versions.

1 Create the space

U-PMS

1. In the sidebar, select `+` next to `Spaces` (or `Spaces` → `Create space`).
2. Choose the `Blank` template (or `Kanban`).
3. Enter the name **U-PMS Rollout** and a key such as **UPR**; choose who can access it.
4. On `Bring your team`, add the people who will work in it, then create the space.

JIRA

1. In the sidebar, select `Spaces` → `+ Create space`.
2. Choose a template (Blank, or Software development → Kanban) → `Use template`.
3. Choose a team-managed space; enter the name **U-PMS Rollout** and the key **UPR**.
4. Add your team when Jira asks, then open the new space.

2 Create the 10 milestone epics

U-PMS

1. Select `+ Create` in the top bar.
2. Open the type menu (it shows `Task`) and choose `Epic`.
3. Type the summary, for example **1. Development**.
4. Set the `Start date` and `Due date` chips from section 4.
5. Tick `Create another` and select `Create`; repeat for all 10 epics.
6. Optional: open each epic and pick a `Color` so the milestones stand apart on the Board and Timeline.

JIRA

1. Select `+ Create` in the top bar.
2. Set `Work type` to `Epic`.
3. Type the summary, for example **1. Development**.
4. Set `Start date` and `Due date` (they may be under more fields).
5. Tick `Create another` and select `Create`; repeat for all 10 epics.
6. Alternative: on the `Timeline`, use `+ Create Epic` at the bottom of the list.

3 Add the tasks under each epic

U-PMS

1. Open the epic (select it on the Board, List or Timeline).
2. In `Child work items`, select `Add child work item`, type the summary and press Enter. Repeat for each task of the milestone.
3. Open each new task and set, in its details: `Start date`, `Due date`, `Assignee`, `Priority` and `Labels`.
4. For building work, change the type to `Story`.
5. Alternative: `+ Create` → `Show all fields` → choose the epic as parent; all fields in one form.

JIRA

1. Open the epic.
2. In `Child work items`, select `+` (Add child work item), type the summary and press Enter.
3. Open each task and set `Start date`, `Due date`, `Assignee`, `Priority` and `Labels` in its details.
4. Change the work type to `Story` where needed.
5. Alternative: `+ Create` and choose the epic in the `Parent` field.

4 Add the sub-tasks

U-PMS

1. Open the task (for example **3.2 Fill out the TDL user creation form...**).
2. In `Child work items`, select `Add child work item`; type the sub-task title and press Enter.
3. Repeat for each sub-task in section 4. Finished ones: `Mark done`.

JIRA

1. Open the task.
2. Select `Add subtask` (or `+` in `Child work items`); type the title and press Enter.
3. Repeat for each sub-task; move finished ones to `Done`.

5 Schedule on the Timeline

U-PMS

1. Open the `Timeline` tab. Each epic is a group with its tasks under it; columns show Work, Status and Assignee.
2. Drag a bar to move its dates; drag either end to change only the start or the due date.
3. A row without dates shows `Schedule` when you point at it; select it to give it dates, then drag.
4. Use `Today`, `Weeks`, `Months`, `Quarters` at the bottom right. Months suits this plan.
5. Keyboard: select a bar and use the arrow keys to move it by a day; Enter saves.

JIRA

1. Open the `Timeline` tab. Epics are rows; expand an epic to see its child work items.
2. Drag a bar to move it; drag its ends to change the start or due date.
3. For a row without dates, point at the chart in that row and click or drag to create the bar.
4. Use `Today`, `Weeks`, `Months`, `Quarters` at the bottom right.

6 Link the dependencies

U-PMS

1. Open the item that has to wait (for example **3.4 Deploy U-PMS to the UAT VM**).
2. In `Linked work items`, select `Add linked work item`.
3. Choose `waits for...` and pick the item from section 4's "Waits for" column (3.2 and 3.3).
4. Or on the Timeline: the row's `···` → `Add dependency`.
5. Arrows join the bars on the Timeline; a dashed red arrow means the dates overlap (late).

JIRA

1. On the Timeline, point at the bar that must finish first; drag the dot at its end onto the bar that waits. Jira records "blocks".
2. Or open the waiting item → `Link work item` → `is blocked by` → pick the item.
3. Arrows join the bars; Jira colours an arrow red when the dates conflict.

7 Set the statuses

U-PMS

1. Board: drag the six finished development stories (1.1 to 1.6) and their sub-tasks to `Done`; drag the epic **1. Development** to `In Progress`.
2. Or open an item and change its status from the status button.

JIRA

1. Board: drag the items to `Done` or `In Progress`.
2. Or open an item and change the status from its status button.

8 Follow the plan

U-PMS

1. **Summary** : counts, status donut, recent activity, team workload and epic progress.
2. **Board** : **Group** → **Epic** shows one swimlane per milestone; the label filter shows one team's tasks.
3. **List** : filter by label (for example `ms-team`) to prepare a follow-up with that team.
4. **Calendar** : due dates by month. **Reports** : created vs resolved, cycle and lead time.

JIRA

1. **Summary** : the same overview sections.
2. **Board** : group by epic for swimlanes; filter by label.
3. **List** : filter by label; save the filter for each team.
4. **Calendar** and **Reports** for dates and progress.

9 Optional: formal approvals

U-PMS

1. Approvals (IT-PMO, UAT sign-off, IS) can be real sign-offs: create the space with the **Stage-gate** template.
2. Make each milestone a stage; set its gate's approvers (for example the IT-PMO head, the Head of Department, IS).
3. The next stage cannot start until the gate is approved; the **Approvals** tab lists what is waiting.

JIRA

1. Approvals on a workflow step need Jira Premium (the Approvals tab shows "Try with Premium").
2. On the standard plan, use a task such as **2.2 Get approval from the IT-PMO department** and record the approval in a comment.

6. Comparison checklist

Note how each step felt in both tools: clicks needed, clarity, speed, and anything missing.

Area	U-PMS	Jira	Your notes
Create the space	Template gallery, then name, key, access and team	Template gallery, then name, key and team	
Create 10 epics	+ Create, type Epic, dates, Create another	+ Create, work type Epic, dates, Create another	
Child tasks under an epic	Epic → Add child work item	Epic → Add child work item	
Sub-tasks	Task → Add child work item	Task → Add subtask	
Dates on items	Start and due date in details or on the Timeline	Start and due date in details or on the Timeline	
Timeline scheduling	Drag bars and ends; Schedule for rows without dates	Drag bars and ends; click a row to add dates	
Dependencies and arrows	Add linked work item (waits for / blocks); arrows, red when late	Drag between bars or Link work item; arrows, red on conflict	
Team labels and filters	Labels on items; filter Board and List	Labels on items; filter Board and List	
Board by milestone	Group by Epic (swimlanes)	Group by epic	
Calendar	Month view; drag to move; + on a day	Month view	
Summary page	Counts, status donut, activity, workload, epic progress	Counts, status, activity, workload, types	
Reports	Status, type and assignee donuts; trends; cycle and lead time	Reports dashboard	
Formal approvals	Stage-gate gates with named approvers; Approvals tab	Workflow approvals on Premium	
Forms and Docs	Built in: Forms create work items; Docs pages	Forms; Docs need Confluence	
Attachments and archive	Attachments view with filters; Archived work items	Attachments view; Archived work items	
Overall time to enter the plan			

Assumptions behind the dates

- Working days are Monday to Friday; public holidays and leave are not included.
- The remaining development work (1.7 to 1.13) finishes by 30 October 2026, before the IT-PMO submission.
- The UAT, Azure repository, LDAP and EDMS tracks (3 to 6) all start on 9 November, the Monday after the IT-PMO approval.
- UAT testing (3.5) waits for the LDAP APIs for UAT (5.5). If UAT can start without LDAP, remove that dependency and UAT can finish around 4 December.
- Each request to another team allows 3 to 7 working days for their reply; adjust these to the teams' real service times.
